COMPTON COMMUNITY COLLEGE DISTRICT
FOOTBALL FIELD SCHEDULE
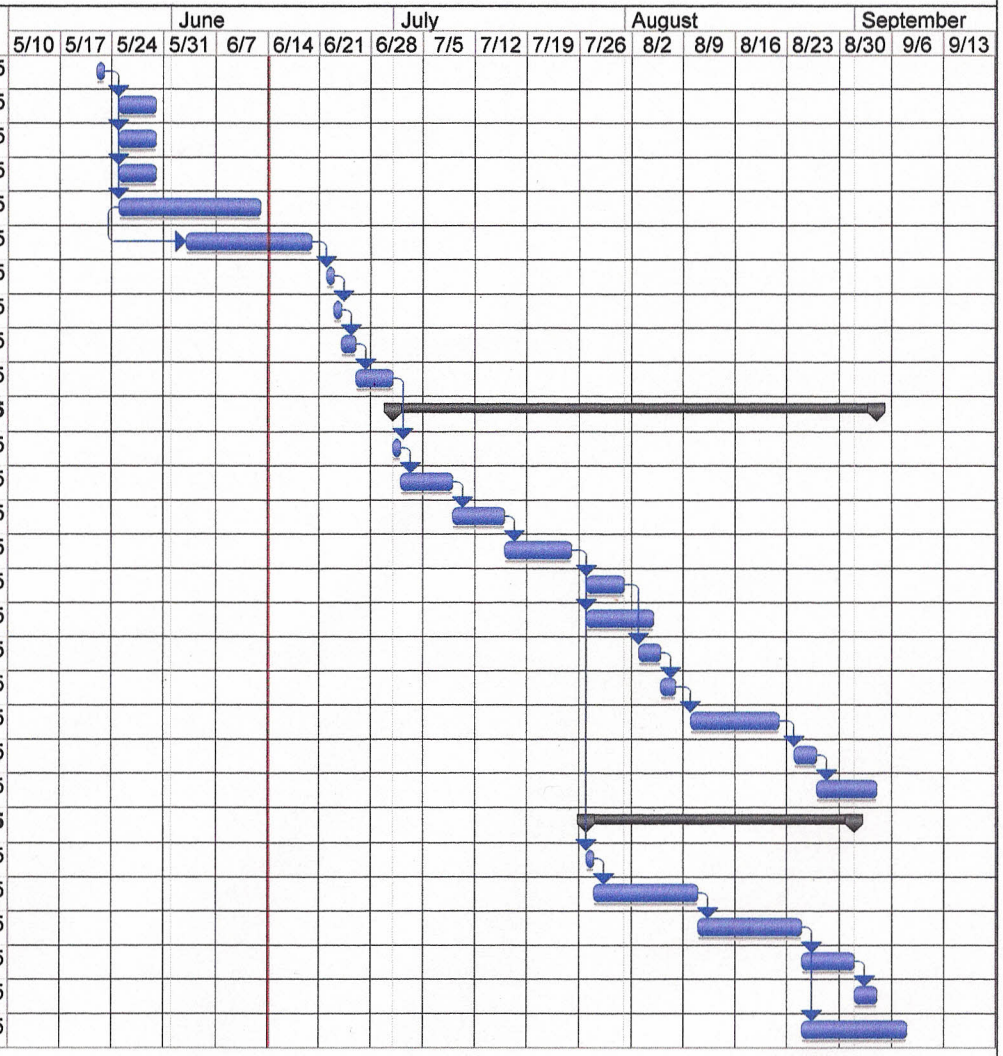
ID	Task Name	Duration	Start	Finish
1	Kick Off Meeting	1 day	Fri 5/22/15	Fri 5/22/15
2	Soils Testing and Report	5 days	Mon 5/25/15	Fri 5/29/15
3	Survey	5 days	Mon 5/25/15	Fri 5/29/15
4	Order Materials	5 days	Mon 5/25/15	Fri 5/29/15
5	Plans & Specs.	15 days	Mon 5/25/15	Fri 6/12/15
6	Short Bid	13 days	Wed 6/3/15	Fri 6/19/15
7	Bid Opening	1 day	Mon 6/22/15	Mon 6/22/15
8	Post Bid Interview	1 day	Tue 6/23/15	Tue 6/23/15
9	Board Approval	2 days	Wed 6/24/15	Thu 6/25/15
10	Execute Contracts	3 days	Fri 6/26/15	Tue 6/30/15
11	**Construction #CCCD-026**	**47 days**	**Wed 7/1/15**	**Thu 9/3/15**
12	Mobilize	1 day	Wed 7/1/15	Wed 7/1/15
13	Grading & Compaction	5 days	Thu 7/2/15	Wed 7/8/15
14	Irrigation & Drainage	5 days	Thu 7/9/15	Wed 7/15/15
15	Base & Asphalt	7 days	Thu 7/16/15	Fri 7/24/15
16	Grading Areas Outside the Field	5 days	Mon 7/27/15	Fri 7/31/15
17	Pumping System	7 days	Mon 7/27/15	Tue 8/4/15
18	Soil Treatment Outside the Field	3 days	Mon 8/3/15	Wed 8/5/15
19	Irrigation Capping Outside Field	2 days	Thu 8/6/15	Fri 8/7/15
20	DG/Pro Gold	10 days	Mon 8/10/15	Fri 8/21/15
21	Fencing Repair	3 days	Mon 8/24/15	Wed 8/26/15
22	Clean Up and Close Out	6 days	Thu 8/27/15	Thu 9/3/15
23	**KYA Contract**	**26 days**	**Mon 7/27/15**	**Mon 8/31/15**
24	Accept Asphalt	1 day	Mon 7/27/15	Mon 7/27/15
25	Drainage Board	10 days	Tue 7/28/15	Mon 8/10/15
26	Football Field	10 days	Tue 8/11/15	Mon 8/24/15
27	Stripping/Clean Up	5 days	Tue 8/25/15	Mon 8/31/15
28	Testing all Systems	3 days	Tue 9/1/15	Thu 9/3/15
29	Warranties & Close Out	10 days	Tue 8/25/15	Mon 9/7/15
